

Brooklyn

Third Quarter 2021

# Replacement of Combined Sewers, Bulkheading of existing Sewers and Water Main Replacement in Park Place.

Brooklyn

The NYC Department of Design and Construction (NYCDDC) is upgrading the infrastructure within Prospect Heights, Brooklyn to improve water drainage and quality. The DDC will install replacements of distribution water mains, install combined sewers, and restore the trenches where the work was performed. The project involves the replacement and/or reconstruction of combined sewers, manholes, chambers, catch basins, distribution water mains and hydrants. This project includes final restoration for all water and sewer trenches, resurfacing with a 2" overlay of asphaltic concrete wearing course, and installation of new streetlights and traffic lights at the intersection of Carlton Avenue and Park Place.

**Current Locations for Work Operations: Tasks to Include water main Installation**

- Intersection of Vanderbilt Avenue and Park Place

**Upcoming Locations for Work Operations:**

- Replacement of existing Watermains:
  - Vanderbilt Avenue between Park Pl and Sterling Place
  - Underhill Avenue between Park Pl and Sterling Place
- Installation of Combined Sewers:
  - Park Avenue between Flatbush Avenue and Vanderbilt Avenue
  - Park Avenue between Vanderbilt Avenue Underhill Avenue
  - Vanderbilt Avenue between Park Pl and Sterling Place
  - Underhill Avenue between Park Pl and Sterling Place
- Installation of Sewer Chamber:
  - At the intersection of Carlton Avenue and Park Place

**Completed Work Operations to Date: Intersection of Vanderbilt Ave. and Park Pl.**


- Replacement of Water Main:
- Replacement of 250 Linear Feet of DIP Watermain
  - Replacement of 1 8" Gate Valve
  - Replacement of 2 12" Gate Valves
  - Replacement of 2 Fire Hydrants

**Community Impacts**

During construction hours, you can expect the following:

- Increased levels of dust, noise, and heavy equipment.
- Vehicular travel lane closures will be required, as well as detours. Warning signs will be posted in advance.
- Parking and driveway/loading dock restrictions, signs will be posted within the affected areas.
- Emergency vehicle access and pedestrian access to sidewalk and buildings will be maintained at all times.

Project # SEK002386

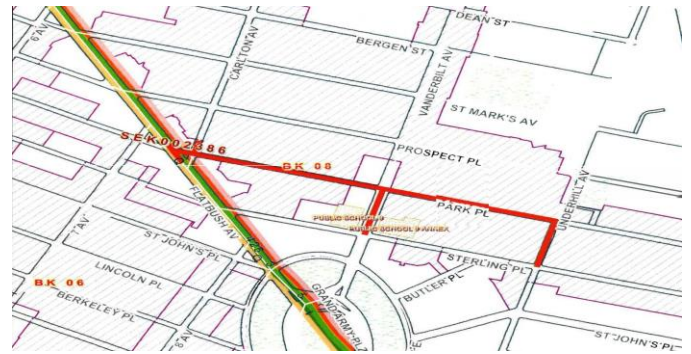

The neighborhood we are working on is Prospect Heights

**Water Service Interruptions**

During the course of the project, there will be service interruptions. To allow water main replacement, the existing water service must be shut off by closing the valves at either end of the section. Advance notice will be given for all planned interruptions. Water service will be restored at the end the workday

**Newsletter Distribution**

Construction Newsletters for this project are distributed regularly within the project area and to Brooklyn Community Board #8

**Special Needs**

Individuals with special needs who may be uniquely impacted by this project should contact the project's Community Construction Liaison, as soon as possible, to make them aware of your situation. DDC will work with you to attempt to minimize the inconvenience as much as possible.

**Property Damage**

You are advised to inform the DDC or the Contractor of any of your property damage that you may have. If the contractor fails to respond within 10 days, you should inform the DDC Borough Director in writing. If you intend to file a claim you must do so within 90 days of the occurrence with the New York City Comptroller's Office.

**Community Construction Liaison (CCL)**

The DDC has assigned **Ahmed Elhashash**, as the Community Construction Liaison (CCL) for this project. Please contact Mr. Elhashash for any project related inquiries/concerns you may have:

Phone: 516.464.0614  
 Email: Parkplccl@gmail.com  
 Field Office: 250 6th Street, Brooklyn, NY 11215
